Estimated Project Schedule - Comal County Habitat Conservation Plan
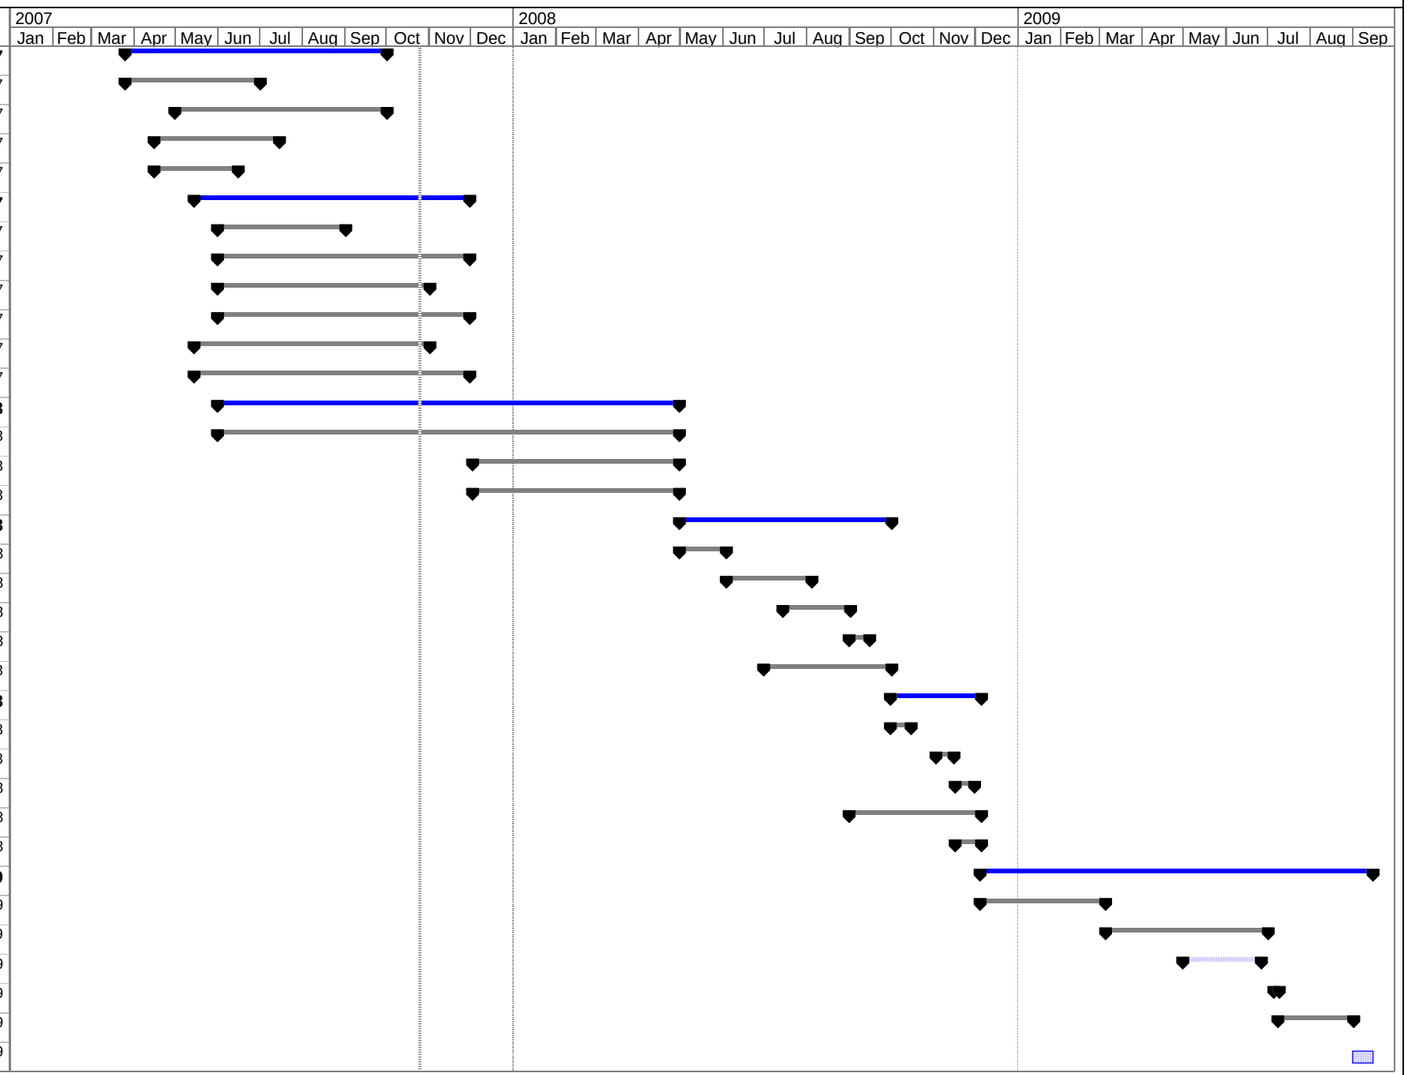
ID	Name	Start	Finish
Phase 1	**Project Organization**	**Mon 3/26/07**	**Mon 10/1/07**
	Early coordination with USFWS, TPWD, and other agencies	Mon 3/26/07	Sun 7/1/07
	Early coordination with stakeholders (potential BAT & CAC members)	Tue 5/1/07	Mon 10/1/07
	Compilation of studies and literature	Mon 4/16/07	Sun 7/15/07
	Summary of legal requirements	Mon 4/16/07	Fri 6/15/07
Phase 2	**Project Development and Community Guidance**	**Tue 5/15/07**	**Fri 11/30/07**
	Formation of Citizens Advisory Committee (CAC)	Fri 6/1/07	Sat 9/1/07
	Formation of Biological Advisory Team (BAT)	Fri 6/1/07	Fri 11/30/07
	Develop Public Outreach/Participation Process	Fri 6/1/07	Thu 11/1/07
	Engage Economist	Fri 6/1/07	Fri 11/30/07
	Baseline Data Acquisition and Preliminary Analysis	Tue 5/15/07	Thu 11/1/07
	Initial Strategy/Framework Development	Tue 5/15/07	Fri 11/30/07
Phase 3	**Prepare Conceptual Draft HCP**	**Fri 6/1/07**	**Wed 4/30/08**
	Prepare complete (but preliminary) draft of HCP	Fri 6/1/07	Wed 4/30/08
	Review and input from Economic Analyst on financial impacts and funding plan for HCP	Mon 12/3/07	Wed 4/30/08
	NEPA (PDEIS Baseline and Alternatives)	Mon 12/3/07	Wed 4/30/08
Phase 4	**Committee/Agency Review and HCP Revision**	**Thu 5/1/08**	**Wed 10/1/08**
	First round of review and revision	Thu 5/1/08	Tue 6/3/08
	Second round of review and revision	Wed 6/4/08	Mon 8/4/08
	NEPA Scoping Process	Tue 7/15/08	Mon 9/1/08
	Solicit approval from Committees and Comm. Court to proceed with Final Draft HCP	Mon 9/1/08	Mon 9/15/08
	NEPA (PDEIS Impacts and Conclusions)	Tue 7/1/08	Wed 10/1/08
Phase 5	**Permit Application**	**Wed 10/1/08**	**Fri 12/5/08**
	Prepare Final Draft HCP for submittal	Wed 10/1/08	Wed 10/15/08
	TPWD Code Public Hearing on HCP	Mon 11/3/08	Sat 11/15/08
	Review and approval of application documents by Comal Co. Comm. Ct.	Mon 11/17/08	Sun 11/30/08
	Prepare and submit Notice of Availability for HCP/EIS	Mon 9/1/08	Fri 12/5/08
	Submit application package (Final Draft HCP, DEIS, application form, application fee)	Mon 11/17/08	Fri 12/5/08
Phase 6	**Permit Processing**	**Fri 12/5/08**	**Tue 9/15/09**
	Public Meeting and Comment Period	Fri 12/5/08	Thu 3/5/09
	Preparation of Final EIS	Fri 3/6/09	Wed 7/1/09
	Prepare and Submit Notice of Availibility for Final HCP/EIS	Fri 5/1/09	Fri 6/26/09
	Submittal of Final EIS	Mon 7/6/09	Thu 7/9/09
	FWS Internal Documents	Thu 7/9/09	Tue 9/1/09
	Permit Issuance	Tue 9/1/09	Tue 9/15/09
